




2020 Street Improvements Northeast Area (Contract 20-101) Construction Updates August 24, 2020

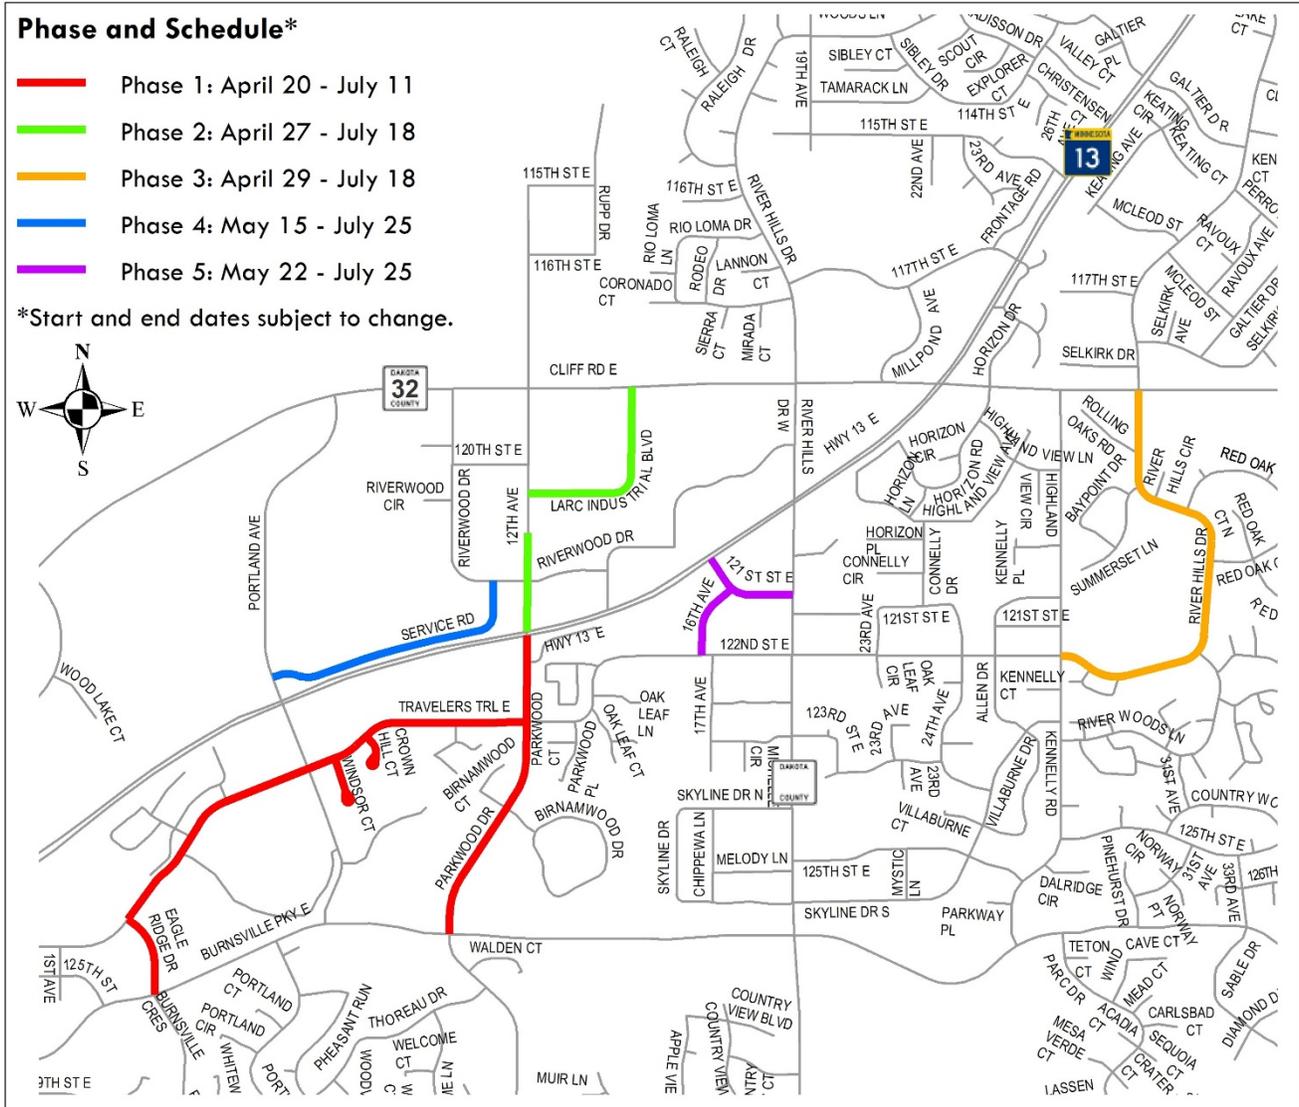

All Phases

Boulevard Restoration:

- A combination of strategies including re-seeding, digging and re-seeding, and application of weed and feed was completed the week of August 17, 2020.
- The City and Contractor will monitor the boulevards for the next few weeks while the weed and feed treatment takes. Additional re-seeding and soil topdressing will occur as-needed around mid-September 2020.

2020 Street Improvements Northeast Area (Contract 20-101) Estimated Schedule by Phase*

	 Start	 Utilities	 Curb	 Grading/Paving	 Restoration	 Complete
Phase 1	Apr 20	Apr 24 – May 8	Apr 30 – May 15	May 4-20	May 18 – Jul 11	Jul 11
Phase 2	Apr 24	May 5-8	May 26 – Jun 23	Jun 29 – Jul 2	Jun 22 – Jul 18	Jul 18
Phase 3	Apr 29	May 5-22	May 26 – Jun 4	May 19 – Jun 18	Jun 25 – Jul 18	Jul 18
Phase 4	May 15	May 18-21	May 28 – Jun 26	Jun 15 – Jul 11	Jul 13-25	Jul 25
Phase 5	May 22	May 26 – Jun 12	Jun 22-27	Jun 30 – Jul 11	Jul 13-25	Jul 25

*Projected dates are subject to change based on weather and contractor operations.

Contact City Inspector Cody Pietz at 952-356-6839 or cody.pietz@burnsvillemn.gov for more information

Subscribe to email and text message updates!

Visit www.burnsvillemn.gov/roadwork and click the “Subscribe” button to sign up for email and/or text message updates.



Subscribe
